



AGENDA REPORT
SAN CLEMENTE CITY COUNCIL MEETING
 Meeting Date: March 6, 2012

Agenda Item 6-D
 Approvals: _____
 City Manager _____
 Dept. Head _____
 Attorney _____
 Finance _____

Department: Public Works / Engineering Division
Prepared By: Ben Parker, Senior Civil Engineer *BP*

Subject: **ACCEPTANCE AND NOTICE OF COMPLETION FOR STREET REHABILITATION ON CALLE SARMENTOSO, PHASE 1 (VIA SOLONA TO CAMINO DEL RIO), PROJECT NO. 11303.**

Summary: The subject contract was awarded to All American Asphalt at the May 3, 2011 meeting of the City Council. The project was completed on time and under the \$700,000 approved budget. The budget includes funding for the entire length of Calle Sarmentoso from Camino Vera Cruz to Camino Del Rio. Phase 2 of the Calle Sarmentoso Rehabilitation from Camino Vera Cruz to Via Solona is being deferred until completion of the planned recycled water line that will be constructed within that portion of Calle Sarmentoso.

The final Calle Sarmentoso Rehabilitation, Phase 1 cost including engineering, inspection, administration and construction is as follows:

Construction Contract	\$298,698
Printing and Advertising	534
Inspection Services (RPO Consulting, Inc.)	14,625
<u>Engineering Design, Admin & Insp.</u>	<u>44,000</u>
Total Project Cost (rounded up)	\$358,000

Recommended Action: STAFF RECOMMENDS THAT THE CITY COUNCIL:

1. Accept the "Street Rehabilitation for Calle Sarmentoso, Phase 1, Project No. 11303," from the Contractor, All American Asphalt;
2. Authorize the Mayor to execute and City Clerk to record the Notice of Completion for the "Street Rehabilitation for Calle Sarmentoso, Phase 1, Project No. 11303,"
3. Authorize the City Clerk to release the Payment Bond 35 days from the recordation of the Notice of Completion upon verification with the Engineering Division that no liens have been levied against All American Asphalt; and
4. Authorize the City Clerk to release the Performance Bond upon receipt of a Warranty Bond in the amount of 25% of the construction cost.


Fiscal Impact: None, the project is within the approved budget.

Attachments: Location Map
Notice of Completion

Notification: None.

i:\engineering\admin\2012 admins\03-06-2012\03-06-12-1r.docx

612

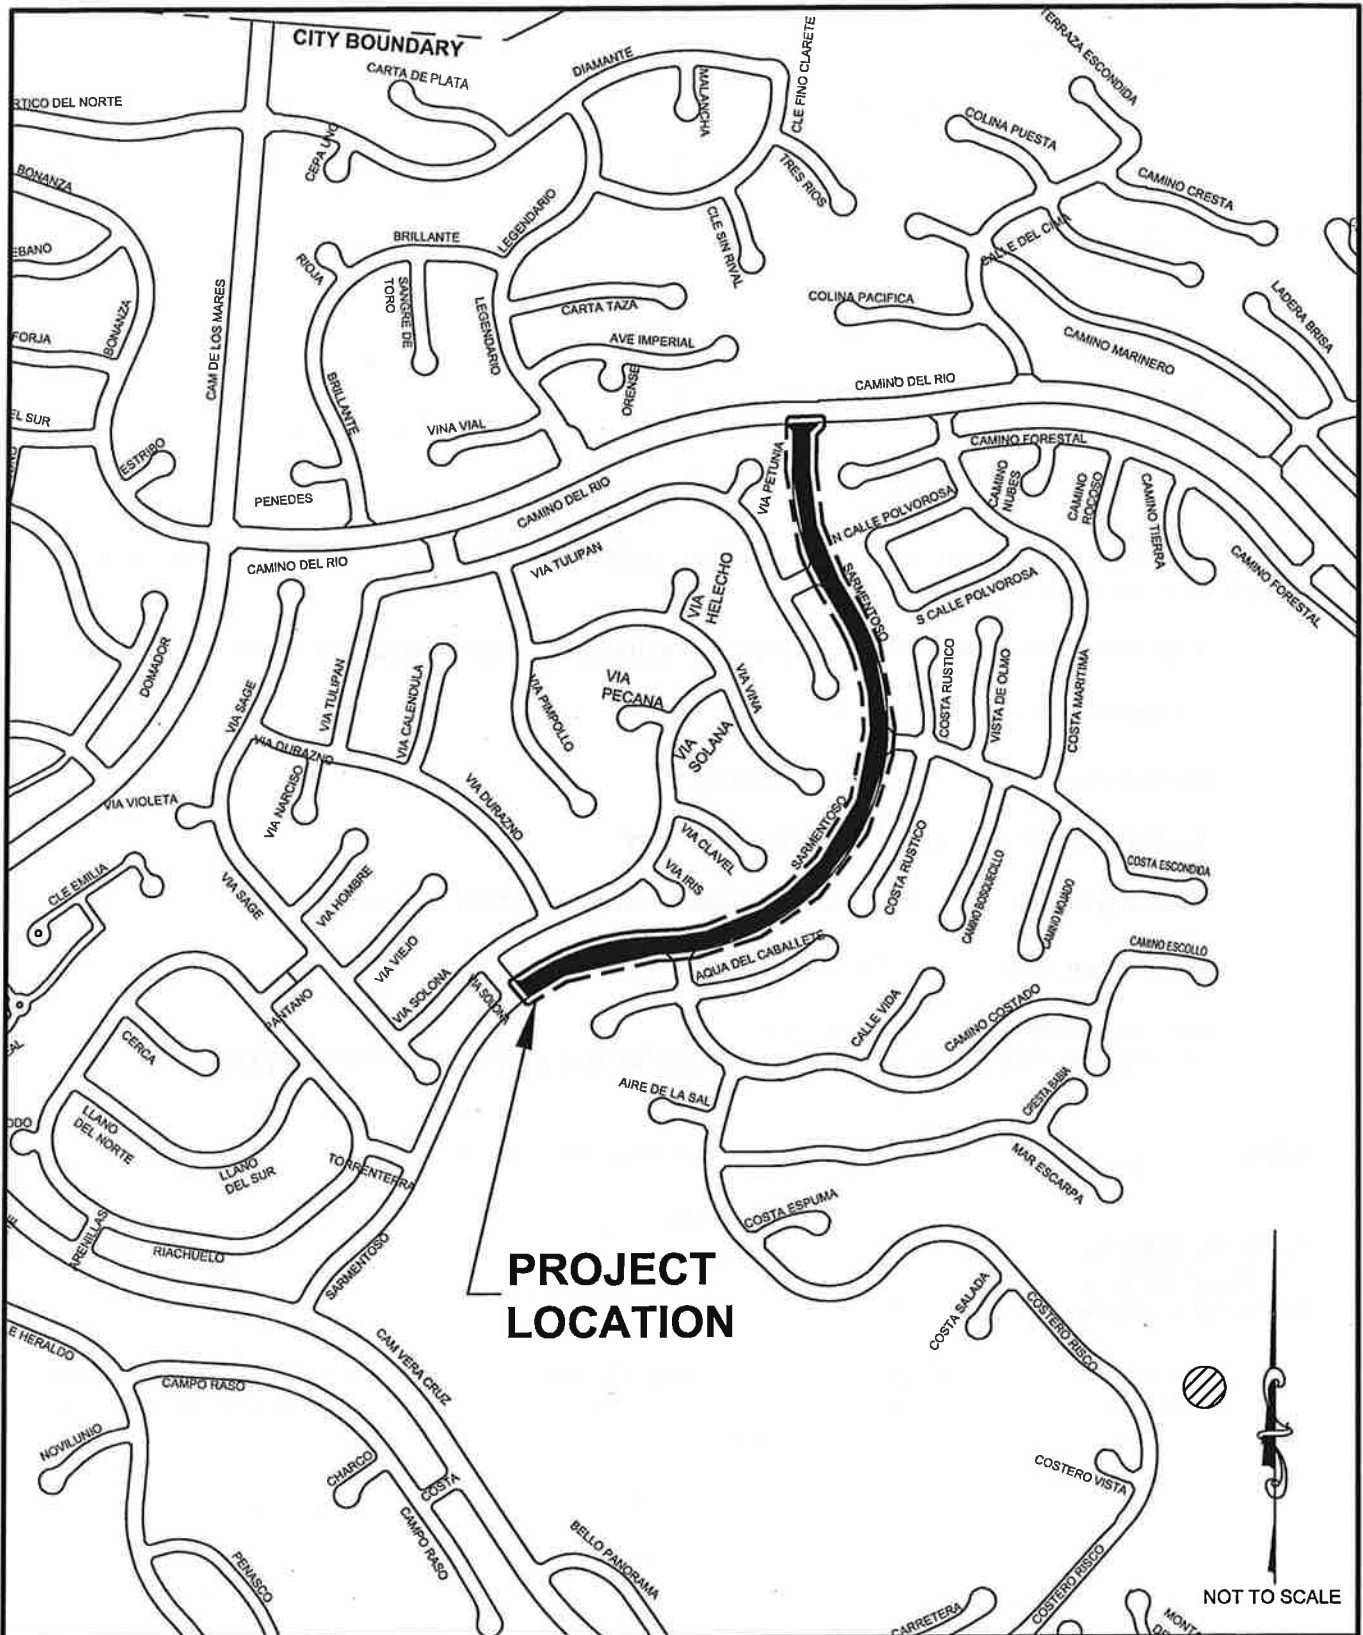

City of San Clemente
 910 Calle Negocio, Suite 100
 San Clemente, CA 92673
 Tel (949) 361-6100
 Fax (949) 361-8316

LOCATION MAP
Calle Sarmientoso
Phase 1
(Via Solona to Camino Del Rio)
PN 11303

(21)-5

<p>Exempt recording requested by the City of San Clemente per Gov. Code Sec. 6103</p> <p>_____ City Clerk</p> <p>When Recorded Mail To:</p> <p>City Clerk City of San Clemente 100 Avenida Presidio San Clemente, CA 92672</p>	
--	--

Space above this line for Recorder's use

NOTICE OF COMPLETION

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed as follows:

Project title or description of work: Street Rehabilitation on Calle Sarmentoso, Phase 1, Project No. 11303

Date of completion: 2-07-12

Name of owner: City of San Clemente

Interest or estate of owner: Public right of way

Address of Owner: 100 Avenida Presidio, San Clemente, California 92672

Name of contractor: All American Asphalt

Street address or legal description of site:
Calle Sarmentoso between Via Solona and Camino Del Rio in the City of San Clemente, California

Dated: _____

Owner: City of San Clemente

Mayor _____

STATE OF CALIFORNIA)
COUNTY OF ORANGE) ss
CITY OF SAN CLEMENTE)

I am the City Clerk of the City of San Clemente, the public entity which executed the foregoing notice, and on whose behalf I make this verification: I have read said notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

City Clerk _____

Dated this ____ day of _____, _____

6D-4
