



AGENDA REPORT

SAN CLEMENTE CITY COUNCIL MEETING
Meeting Date: March 21, 2017

Agenda Item CeD

Approvals:

City Manager [Signature]

Dept. Head [Signature]

Attorney [Signature]

Finance [Signature]

Department: Public Works / Engineering IB
Prepared By: Ben Parker, Senior Civil Engineer

Subject: *CITY COUNCIL ACCEPTANCE AND NOTICE OF COMPLETION FOR STREET REHABILITATION FOR AVENIDA VAQUERO, PROJECT NOS. 11302 AND 13311.*

Fiscal Impact: None. The project was completed within the approved combined budget of \$2,001,000. Of this amount \$880,000 is from the Street Improvement Program Fund and \$1,121,000 is from the Gas Tax Fund.

Summary: R.J. Noble has completed the construction contract on time, within budget and staff recommends Council acceptance.

Discussion: The contract was awarded by the City Council on September 16, 2014. This project included pavement rehabilitation and striping for Avenida Vaquero from Camino Capistrano to Camino De Los Mares. The rehabilitation included reconstructing localized failed pavement areas, cold milling edges, constructing a sub-drain at the eastern edge of pavement where needed and providing a two-inch overlay of rubberized asphalt concrete for the entire length of the roadway. Curb ramps were reconstructed or retrofitted as required by law. The restriping included modifications that balanced the roadway for all the users in conformance with the Centennial General Plan.

Shortly after the paving was completed, Caltrans began widening the I-5 bridge over Avenida Vaquero. In order to minimize the likelihood of damaging new pavement on Avenida Vaquero from construction activities, staff delayed the portion of the overlay surrounding the bridge area until the widening project was complete.

The construction damaged the pavement under the I-5 bridge as expected. However, in addition, the new pavement from the I-5 freeway to Calle Vallarta was damaged from Caltrans trucks hauling large loads of equipment and materials. To address that safety issue the City performed repair work, and recently received a reimbursement for that work under an agreement approved by the City Council. The remaining pavement work near the I-5 bridge will be done under a separate City project in the near future.

A summary of total projects expenditures is provided below:

Construction	\$1,687,875
Design, Admin., Construction Management & Inspection	\$ 165,000
Total Project Cost (rounded up)	\$1,853,000

Recommended


Action: STAFF RECOMMENDS THAT the City Council:

1. Accept the Street Rehabilitation for Avenida Vaquero, Project Nos. 11302 & 13311 from the Contractor, R.J. Noble Company;
2. Authorize the Mayor to execute and the City Clerk to record the Notice of Completion for the Street Rehabilitation for Avenida Vaquero, Project Nos. 11302 & 13311;
3. Authorize the City Clerk to release the Payment Bond 35 days from the recordation of the Notice of Completion upon verification with the Engineering Division that no liens have been levied against the Contractor, R.J. Noble Company; and
4. Authorize the City Clerk to release the Performance Bond upon receipt of a Warranty Bond in the amount of 25% of the construction cost.

Attachments: 1. Location Map
2. Notice of Completion

Notification: None.

i:\cde\engineering\secure\projects\pn_13311 & 11302_upper & lower vaquero imp\06-admin_report\cadd\location map.dwg 12.6.2016

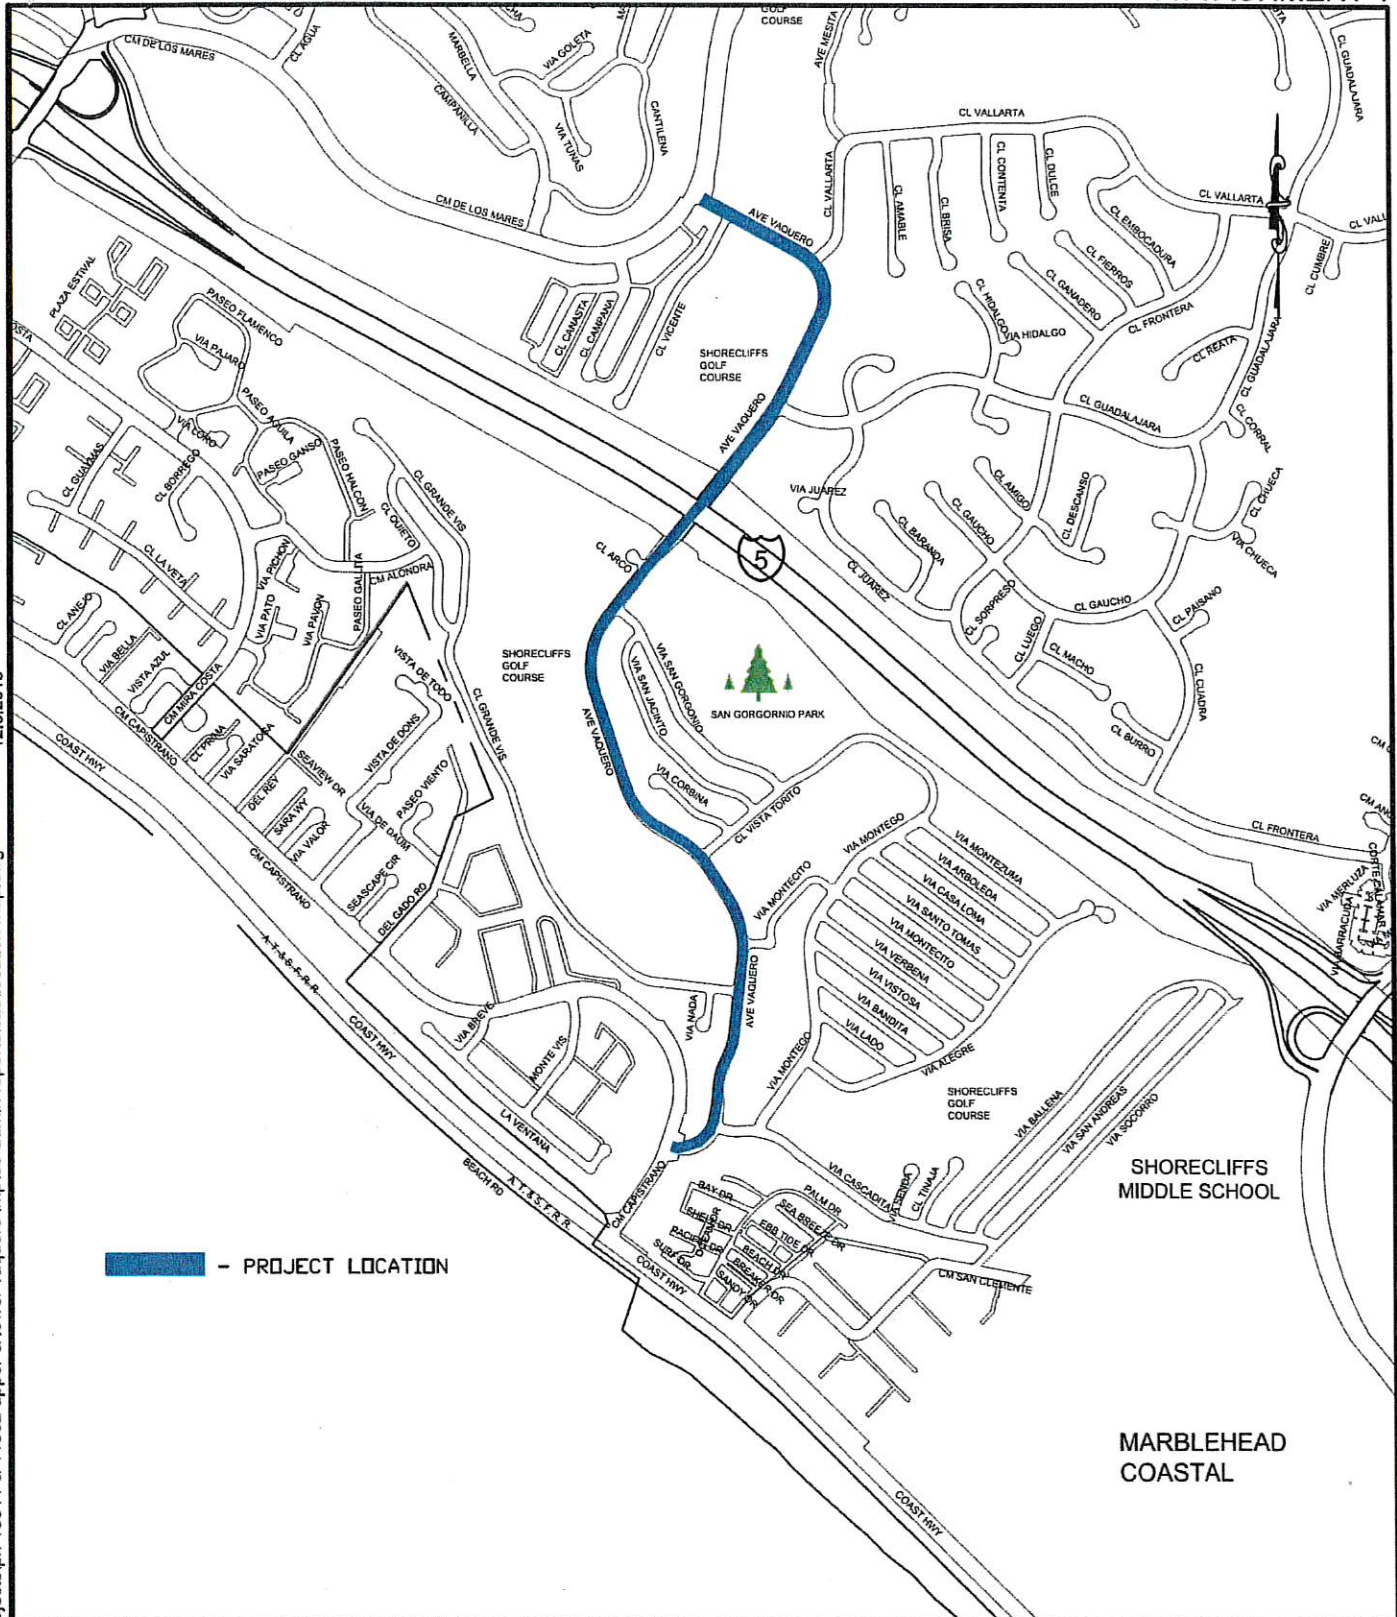

CITY OF SAN CLEMENTE
 910 CL Negocio, Suite 100
 San CLEMENTE, CA 92673
 Tel (949) 361-6100
 Fax (949) 361-8316

LOCATION MAP
 AVENIDA VAQUERO REHABILITATION
 CAMINO CAPISTRANO TO CAMINO DE LOS MARES
 PROJECT Nos. 11302 & 13311

Attachment 2

Exempt recording requested by the City of San Clemente per Gov. Code Sec. 6103 _____ City Clerk	
When Recorded Mail To: City Clerk City of San Clemente 100 Avenida Presidio San Clemente, CA 92672	

Space above this line for Recorder's use

NOTICE OF COMPLETION

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed as follows:

Project title or description of work: Street Rehabilitation for Avenida Vaquero (Camino Capistrano to Camino De Los Mares) Project Nos. 11302 and 13311

Date of completion: January 19, 2015

Name of owner: City of San Clemente

Interest or estate of owner: Public right of way

Address of Owner: 910 Calle Negocio, San Clemente, CA 92673

Name of contractor: R.J. Noble

Street address or legal description of site: Avenida Vaquero (Camino Capistrano to Camino De Los Mares)

Dated: _____

Owner: City of San Clemente

Mayor _____

STATE OF CALIFORNIA)
COUNTY OF ORANGE) ss
CITY OF SAN CLEMENTE)

I am the City Clerk of the City of San Clemente, the public entity which executed the foregoing notice, and on whose behalf I make this verification: I have read said notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

City Clerk _____

Dated this ____ day of _____, _____
