

AGENDA REPORT

SAN CLEMENTE CITY COUNCIL MEETING Meeting Date: August 4, 2015

Agenda Item

Approvals:

City Manager

Dept. Head

Attorney

Finance

Department:

Public Works / Engineering

Prepared By:

Ben Parker, Senior Civil Engineer

Tom Frank, Transportation Engineering Manager

Subject:

CITY COUNCIL ACCEPTANCE AND NOTICE OF COMPLETION FOR CALLE FRONTERA REHABILITATION, FROM AVENIDA PICO TO AVENIDA VISTA HERMOSA, PROJECT NO. 15315.

Fiscal Impact:

None. The total project cost including engineering, inspection, administration and construction is \$561,900 which is within the \$1,200,000 budgeted in the Street

Improvement Fund.

Summary:

All American Asphalt has completed the street rehabilitation contract on time, within budget and staff recommends Council acceptance for:

Street Improvement Program

Calle Frontera (Avenida Pico to Avenida Vista Hermosa), Project No. 15315.

Background:

The contract was awarded by the City Council on January 20, 2015. The entire pavement area was cold-planed two and one-half inches. Afterward, failed pavement areas were reconstructed with six inches of Asphalt Concrete (A.C.) base over geotextile fabric. Following the needed repairs, the entire pavement area was overlaid with a one-inch A.C. leveling course and two-inches of rubberized asphalt. Curb ramps were reconstructed/retrofitted as required to meet current ADA requirements. Also, curb and gutter and local depressions were replaced as needed. The streets were restriped and the crosswalks at the Calle Frontera and Avenida Vista Hermosa intersection were upgraded to "ladder style" with white thermoplastic per City Council direction.

Discussion:

The final cost including engineering, inspection, administration and construction is \$561,900. The budgeted amount is \$1,200,000 from the Street Improvement Fund. The detailed final cost for this project is shown on the Attachment 3. The lower costs were due to lower than estimated pavement replacement quantities, and less design and construction issues than anticipated as a result of an improved design procedure for determining the required pavement removal limits.

Recommended

Action:

STAFF RECOMMENDS THAT the City Council:

1. Accept the Calle Frontera Rehabilitation, Project No. 15315 from the Contractor, All American Asphalt:

- 2. Authorize the Mayor to execute and the City Clerk to record the Notice of Completion for the Calle Frontera Rehabilitation, Project No.15315;
- 3. Authorize the City Clerk to release the Payment Bond 35 days from the recordation of the Notice of Completion upon verification with the Engineering Division that no liens have been levied against the Contractor, All American Asphalt; and
- 4. Authorize the City Clerk to release the Performance Bond upon receipt of a Warranty Bond in the amount of 25% of the construction cost.


Attachments:

- 1. Location Map
- 2. Notice of Completion
- 3. Detailed Final Cost Estimate

Notification: None.

i:\cd\engineering\secure\admin\2015 admins\08-04-2015\8-4-15-5r.docx

8-4-15 / 6F-3

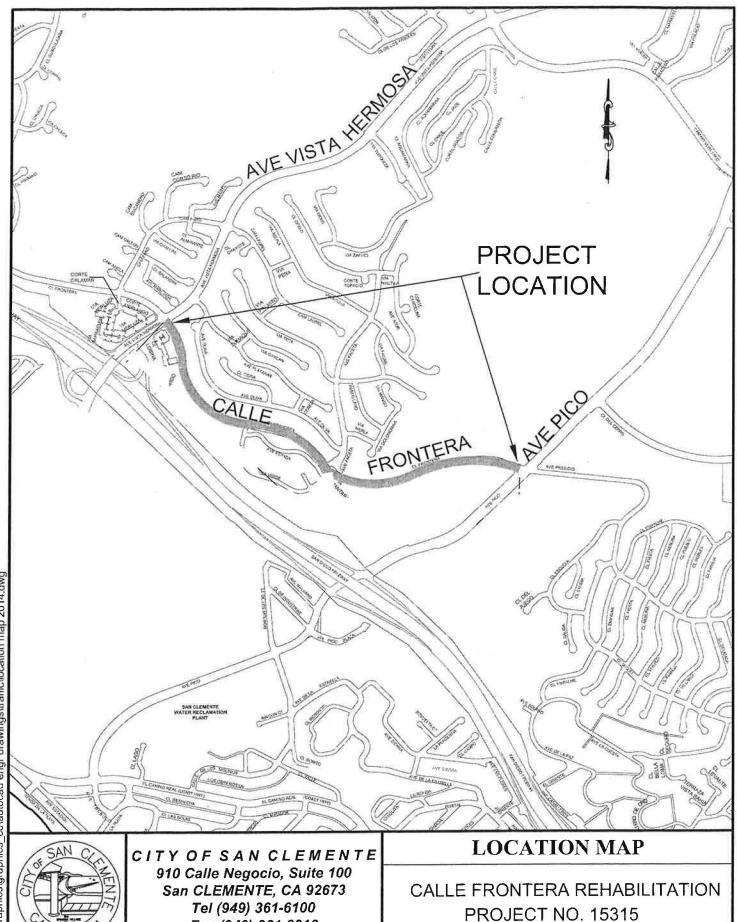

Fax (949) 361-8316

\lcfgraphics\graphics_cd\autocad engr drawings\traffic\location map 2014.dwg

Attachment 2

Exempt recording requested by the City of San Clemente per Gov. Code Sec. 6103	
City Clerk	
When Recorded Mail To:	
City Clerk City of San Clemente 100 Avenida Presidio San Clemente, CA 92672	
	Space above this line for Recorder's use
NOTICE OF C	COMPLETION
Notice is hereby given by the undersigned owner, of improvement has been completed as follows:	a public entity of the State of California, that a public work
Project title or description of work: Calle Front	era Rehabilitation, Project No. 15315
Date of completion: June 12, 2015	
Name of owner: City of San Clemente	
Interest or estate of owner: Public Right of Way	
Address of Owner: 100 Avenida Presidio, San C	Clemente, CA 92672
Name of contractor: All American Asphalt	
	ra (Avenida Pico to Avenida Vista Hermosa) ente, California.
Dated: Ow	ner: City of San Clemente
STATE OF CALIFORNIA) COUNTY OF ORANGE) ss CITY OF SAN CLEMENTE)	
I am the City Clerk of the City of San Clemente, t whose behalf I make this verification: I have read said no penalty of perjury that the foregoing is true and correct.	he public entity which executed the foregoing notice, and on tice, know its contents, and the same is true. I certify under
City	Clerk
Dat	ed this day of
STATE OF CALIFORNIA) COUNTY OF ORANGE) ss CITY OF SAN CLEMENTE) I am the City Clerk of the City of San Clemente, t whose behalf I make this verification: I have read said no penalty of perjury that the foregoing is true and correct. City	he public entity which executed the foregoing notice, and tice, know its contents, and the same is true. I certify un

Attachment 3

DETAILED COST ESTIMATE FOR PROJECT ACCEPTANCE

	Construction	Administration Inspection, Construction Mgt.	Cost (Rounded Up)		
Street Improvement (042)	\$ 508,830	\$ 53,061	\$ 561,900	\$ 1,200,000	\$ 638,10
