

AGENDA REPORT

Agenda Item Approvals: City Manager Dept. Head Attorney Finance

SAN CLEMENTE CITY COUNCIL MEETING Meeting Date: September 5, 2017

Department:

Public Works / Engineering

Prepared By:

Ben Parker, Senior Civil Engineer

Subject:

CITY COUNCIL ACCEPTANCE AND NOTICE OF COMPLETION FOR FY 2017 MAJOR STREET MAINTENANCE FOR AVENIDA ORTEGA, CALLE DEL CERRITO, ARDILLA LANE, CALLE GOMEZ, CALLE DEL RITO, EAST AVENIDA MAGDALENA, LOS BAUTISMOS LANE. AND VARIOUS OTHER PAVEMENT REPAIR LOCATIONS, PROJECT NOS. 27305 AND 27306.

Fiscal Impact: None. The total project cost including engineering, inspection, administration and construction is \$503,000 which is within the combined approved budget of \$717,000 in the FY 2017 Gas Tax, Street Improvement and Water Funds.

Summary:

All American Asphalt has completed the construction contract on time, within budget and staff recommends Council acceptance:

Background/ Discussion:

The contract was awarded by the City Council on August 2, 2016. To receive better bid prices for small isolated pavement repairs, the bid package combined several projects.

Maintenance Streets: This project resurfaced streets shown on the location map provided in Attachment 1 which include: Avenida Ortega, Calle Del Cerrito, Ardilla Lane, Calle Gomez, Calle Del Rito, East Avenida Magdalena and Los Bautismos Lane. The entire street widths were cold milled 1.5 inches followed by reconstructing failed areas. The entire area was overlaid with 1.5 inches of asphalt concrete and restriped.

Various Other Payement Repair Locations: Numerous locations in the southeast quadrant of the City have isolated failed pavement areas of varying size. Approximately 80 of these areas were reconstructed. The method of reconstruction varied depending on the location.

Pavement Repairs Around Water Valves: At the request of the water department, this project also included reconstructing pavement areas at 43 locations throughout the City where water valves have been recently replaced. The method of reconstruction varied depending on the location.

A summary of the total expenditures is provided below:

Construction \$480,734 Administration, Construction Management & Inspection (4.6%) 22.000 Total Project Cost (rounded up) \$503,000

Recommended

Action:

STAFF RECOMMENDS THAT the City Council:

- Accept the FY 2017 Major Street Maintenance for Avenida Ortega, Calle Del Cerrito, Ardilla Lane, Calle Gomez, Calle Del Rito, East Avenida Magdalena, Los Bautismos Lane, and various other pavement repair locations Project Nos. 27305 and 27306 from the Contractor, All American Asphalt;
- Authorize the Mayor to execute and the City Clerk to record the Notice of Completion for FY 2017 Major Street Maintenance for Avenida Ortega, Calle Del Cerrito, Ardilla Lane, Calle Gomez, Calle Del Rito, East Avenida Magdalena, Los Bautismos Lane, and various other pavement repair locations Project Nos. 27305 and 27306;
- 3. Authorize the City Clerk to release the Payment Bond 35 days from the recordation of the Notice of Completion upon verification with the Engineering Division that no liens have been levied against the Contractor, All American Asphalt; and
- 4. Authorize the City Clerk to release the Performance Bond upon receipt of a Warranty Bond in the amount of 25% of the construction cost.


Attachments:

- 1. Location Map
- 2. Notice of Completion

Notification:

None.

s:\cd\engineering\secure\admin\2017 admins\9-5-17\9-5-17-1r.docx

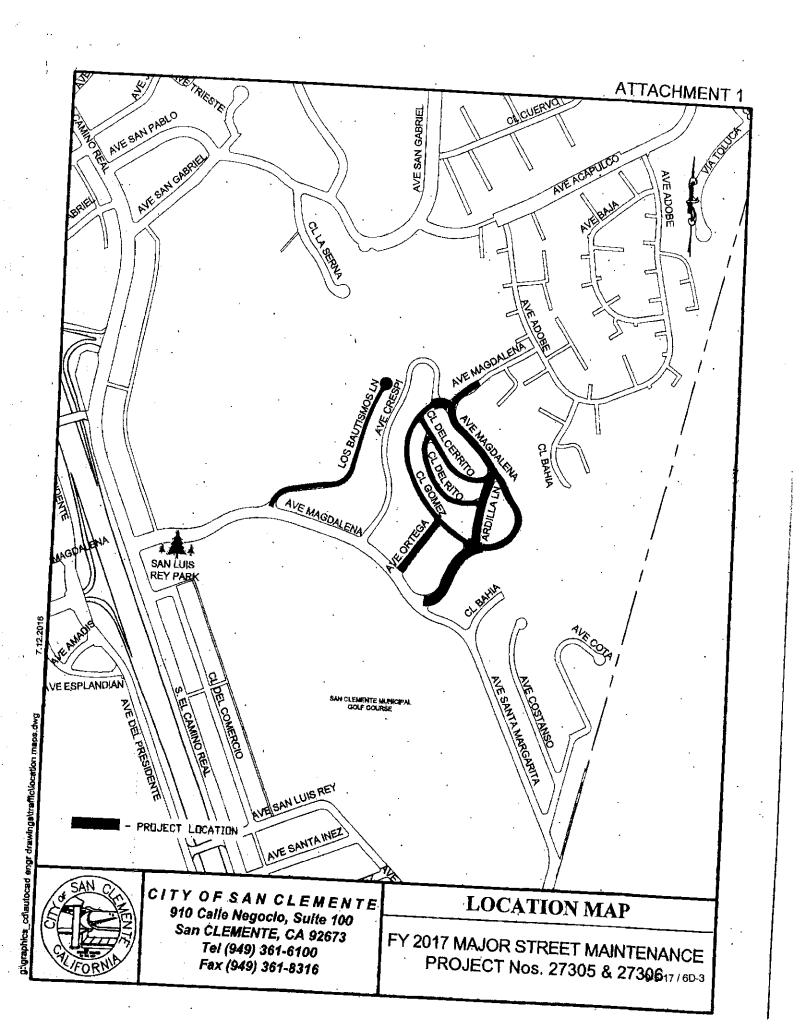

Attachment 2

Exempt recording requested by		
City of San Clemente per Gov. C	Code Sec. 6103	
	City Cleri	rk .
When Recorded Mail To:		• •
City Clerk		
City of San Clemente		
100 Avenida Presidio		·
San Clemente, CA 92672	.	
		Space above this line for Recorder's use
•	NOTIC	CE OF COMPLETION
Notice is hereby given by of improvement has been completed		d owner, a public entity of the State of California, that a public work
Cerrito, Ardilla Lane, C	alle Gomez, Ca	2017 Major Street Maintenance for: Avenida Ortega, Calle Del alle Del Rito, East Avenida Magdalena, Los Bautismos Lane and s City Project Nos. 27305 and 27306
Date of completion: May	31, 2017	
Name of owner: City of	San Clemente	
Interest or estate of owner	r: Public right	of way
Address of Owner: 910 C	caile Negocio, S	San Clemente, CA 92673
Name of contractor: All A	American Asph	aalt ·
		: Avenida Ortega, Calle Del Cerrito, Ardilla Lane, Calle Gomez, ena, Los Bautismos Lane, and various other pavement repair
Dated:		Owner: City of San Clemente
		Mayor
STATE OF CALIFORNIA COUNTY OF ORANGE) ss	
CITY OF SAN CLEMENTE) (
	on: I have read	mente, the public entity which executed the foregoing notice, and on said notice, know its contents, and the same is true. I certify under rect.
	•	City Clerk
		Dated thisday of,

 $i; \label{lem:condition} it is considered a distribution of the completion of the$
