



# AGENDA REPORT

SAN CLEMENTE CITY COUNCIL MEETING  
Meeting Date: April 2, 2019

Agenda Item 6E

**Approvals:**

City Manager [Signature]

Dept. Head [Signature]

Attorney [Signature]

Finance [Signature]

**Department:** Public Works / Engineering  
**Prepared By:** Darra Koger, Senior Civil Engineer

**Subject:** *CITY COUNCIL ACCEPTANCE AND NOTICE OF COMPLETION FOR FISCAL YEAR 2018 MAJOR MAINTENANCE PROJECT NO. 28301*

**Fiscal Impact:** No. The project was completed within the approved budget of \$718,500.

**Summary:** R.J. Noble has completed the construction contract within budget and staff recommends Council acceptance.

**Background:** The contract was awarded by the City Council on August 21, 2018, to complete the Fiscal Year 2018 (FY2018) Major Maintenance projects that included grinding and overlaying the streets identified in Attachment 1. Additionally, \$50,000 of asphalt repair work was included in the project to address required repairs at the intersection of Avenida Vaquero and Camino Capistrano.

A summary of the project expenditures is provided below:

Planning & Design (Rounded up)	\$8,000
Total Construction (Rounded up)	637,000
Construction Management (Rounded up)	11,000
Dudek Consultant Inspection (Rounded up)	14,000
<u>Total Project Cost (Rounded up)</u>	<u>\$670,000</u>

The project was completed February 7, 2019.

**Recommended**

**Action:** STAFF RECOMMENDS THAT the City Council:

1. Accept the Major Street Maintenance FY2018, Project No. 28301 from R.J. Noble Company;
2. Authorize the Mayor to execute and the City Clerk to record the Notice of Completion for the Major Street Maintenance FY2018, Project No. 28301;
3. Authorize the City Clerk to release the Payment Bond 35 days from the recordation of the Notice of Completion upon verification with the Engineering Division that no liens have been levied against the Contractor, R.J. Noble Company; and


4. Authorize the City Clerk to release the Performance Bond upon receipt of a Warranty Bond in the amount of 25% of the construction cost.

**Attachments:** 1. Location Map  
2. Notice of Completion

**Notification:** None.

I:\cd\Engineering\secure\Admin\2019\4-2-19\4-2-19-2r.docx

I:\c:\engineering\secure\projects\p28301 - fy 18 major street maintenance\06-admin reports\cad\location map.dwg 8-4-2017

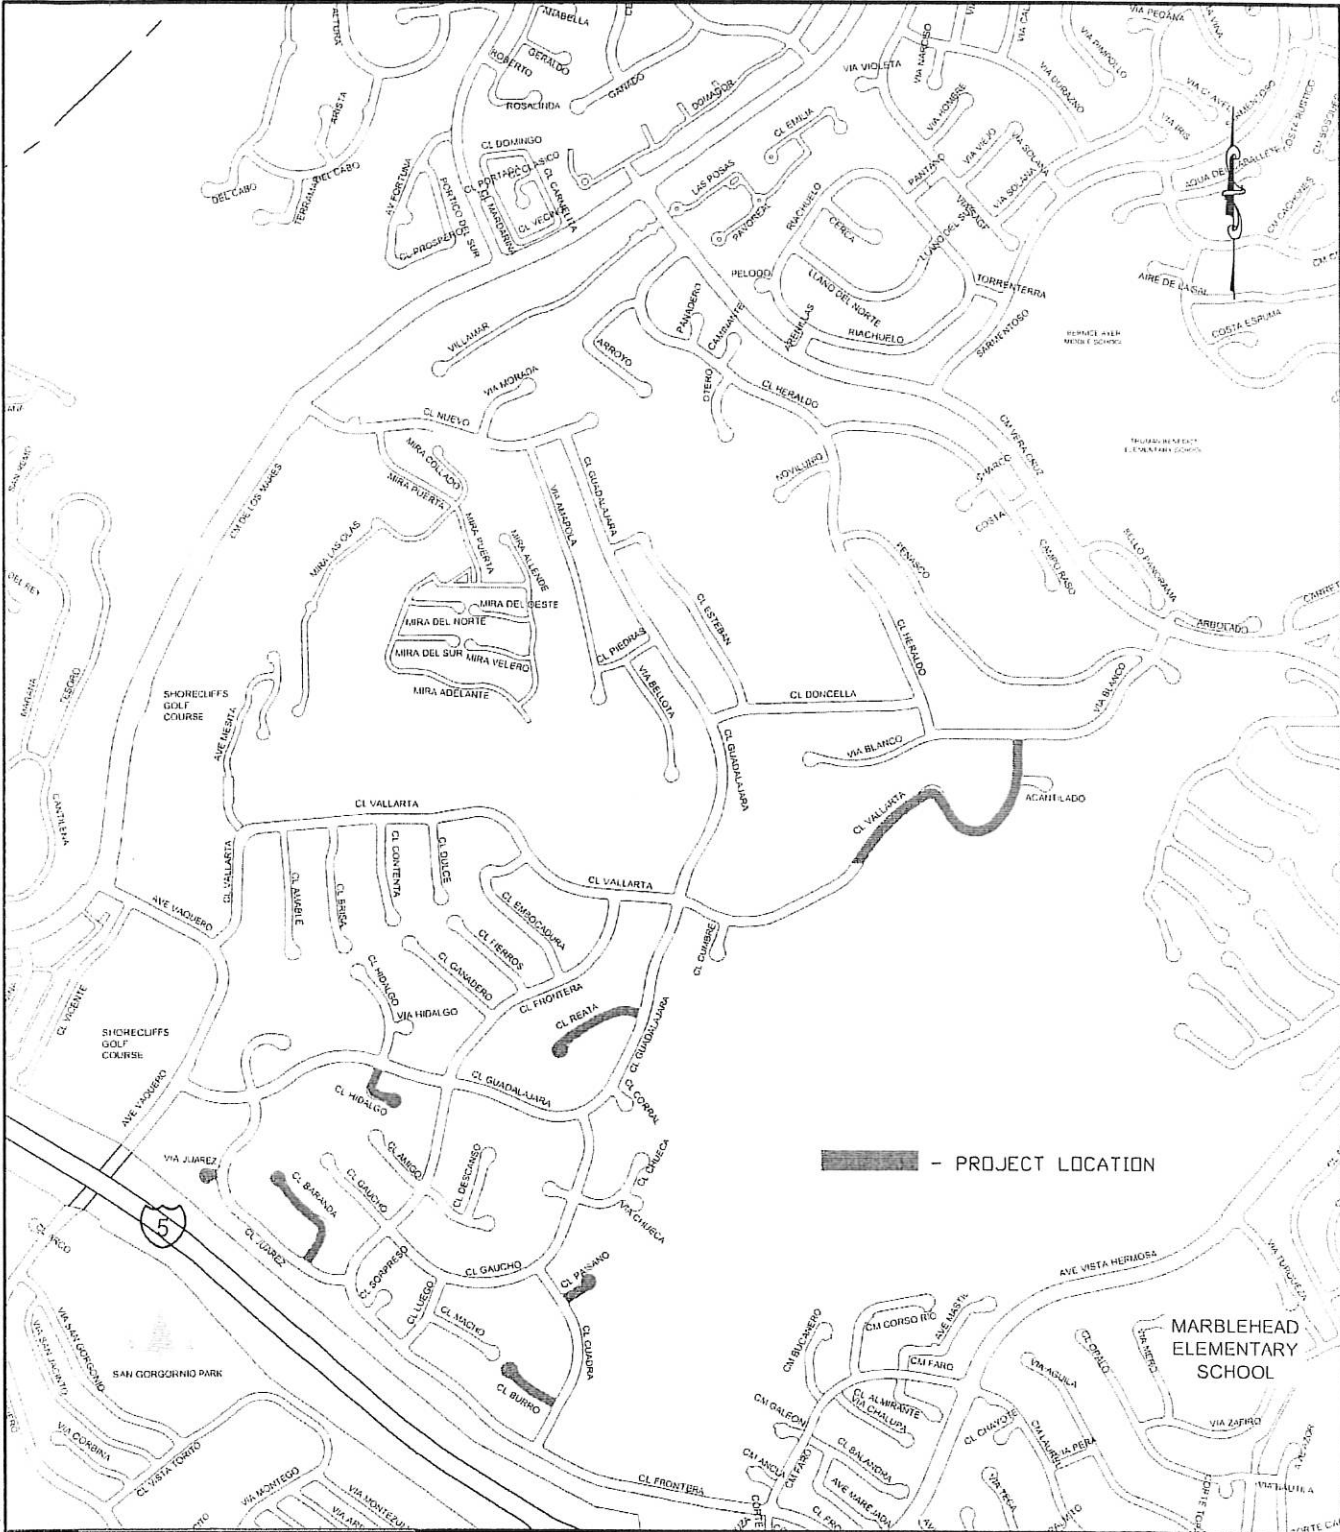

**CITY OF SAN CLEMENTE**  
 910 CL Negocio, Suite 100  
 San CLEMENTE, CA 92673  
 Tel (949) 361-6100  
 Fax (949) 361-8316

**LOCATION MAP**  
 FY 2018 MAJOR STREET MAINTENANCE  
 CALLE BARANDA, CALLE BURRO, CALLE PAISANO,  
 CALLE REATA, CALLE HIDALGO, VIA JUAREZ AND CALLE VALLARTA  
 PROJECT No. 28301

<p>Exempt recording requested by the City of San Clemente per Gov. Code Sec. 27383</p> <p>_____ City Clerk</p> <p>When Recorded Mail To:</p> <p>City Clerk City of San Clemente 100 Avenida Presidio San Clemente, CA 92672</p>	
---	--

Space above this line for Recorder's use

**NOTICE OF COMPLETION**

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed as follows:

***Project title or description of work:*** Major Street Maintenance FY2018, Project No. 28301 and Camino Capistrano Street Project No. 17334

***Date of completion:*** February 14, 2019

***Name of owner:*** City of San Clemente

***Interest or estate of owner:*** Public right of way

***Address of Owner:*** 910 Calle Negocio, San Clemente, CA 92673

***Name of contractor:*** R.J. Noble Company

***Street address or legal description of site:*** Calle Vallarta, Calle Reata, Calle Hidalgo, Via Juarez, Calle Baranda, Calle Burro, and Calle Paisano

Dated: \_\_\_\_\_

Owner: City of San Clemente

Mayor \_\_\_\_\_

STATE OF CALIFORNIA        )  
COUNTY OF ORANGE        ) ss  
CITY OF SAN CLEMENTE     )

I am the City Clerk of the City of San Clemente, the public entity which executed the foregoing notice, and on whose behalf I make this verification: I have read said notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

City Clerk \_\_\_\_\_

Dated this \_\_\_\_ day of \_\_\_\_\_, \_\_\_\_\_
