



Approvals:

City Manager MM

Dept. Head WJ

Attorney ES

Finance SW

AGENDA REPORT

SAN CLEMENTE CITY COUNCIL MEETING
Meeting Date: March 15, 2016

Department: Public Works / Engineering OB
Prepared By: Ben Parker, Senior Civil Engineer

Subject: ***CITY COUNCIL ACCEPTANCE AND NOTICE OF COMPLETION FOR STREET REHABILITATION AND SLURRY SEAL FOR AVENIDA LA PATA, FROM VIA ONDA TO CALLE EXTREMO, PROJECT NO. 15312.***

Fiscal Impact: None. The total project cost including engineering, inspection, administration and construction is \$674,000 which is within the \$757,000 budgeted in the FY15 Gas Tax Fund.

Summary: All American Asphalt has completed the construction contract on time, within budget and staff recommends City Council acceptance of the project.

Background: The contract was awarded by the City Council on June 16, 2015. The project included replacing/retrofitting curb ramps as needed to comply with the Americans with Disabilities Act (ADA). It also originally included cold milling the full street width and a two-inch asphalt overlay. However during internal design coordination, the existing recycle water pipeline under Avenida La Pata was identified as needing replacement within about five years. Given this and the desire to avoid trenching into a relatively new asphalt overlay, executive management staff concurred with a revised repair approach to maintain the pavement condition until the replacement is complete. To achieve this, the full width cold milling and overlay between Avenida Pico and Calle Extremo was reduced to making localized asphalt repairs, installing a leveling course of asphalt, and applying a full width slurry seal. Upon completing the pavement improvements the street was restriped to include buffered bicycle lanes as approved by the City Council in June 2015.

Discussion: The final cost for this project is as follows:

Construction	\$618,464
Engineering, Admin., Const. Mgmt. & Inspection (9%)	\$55,500
Total Project Cost (rounded up)	\$674,000

The \$674,000 total project cost is lower than the budgeted \$757,000 due to the reduction of project scope as explained above.

Recommended


Action: STAFF RECOMMENDS THAT the City Council:

1. Accept the Street Rehabilitation and Slurry Seal for Avenida La Pata, from Via Onda to Calle Extremo, Project No. 15312 from the Contractor, All American Asphalt;
2. Authorize the Mayor to execute and the City Clerk to record the Notice of Completion for the Street Rehabilitation and Slurry Seal for Avenida La Pata, from Via Onda to Calle Extremo, Project No. 15312;
3. Authorize the City Clerk to release the Payment Bond 35 days from the recordation of the Notice of Completion upon verification with the Engineering Division that no liens have been levied against the Contractor, All American Asphalt; and
4. Authorize the City Clerk to release the Performance Bond upon receipt of a Warranty Bond in the amount of 25% of the construction cost.

Attachments: 1. Location Map
2. Notice of Completion

Notification: None.

i:\cd\engineering\secure\admin\2016 admin\3-15-16\3-15-16-6r.docx

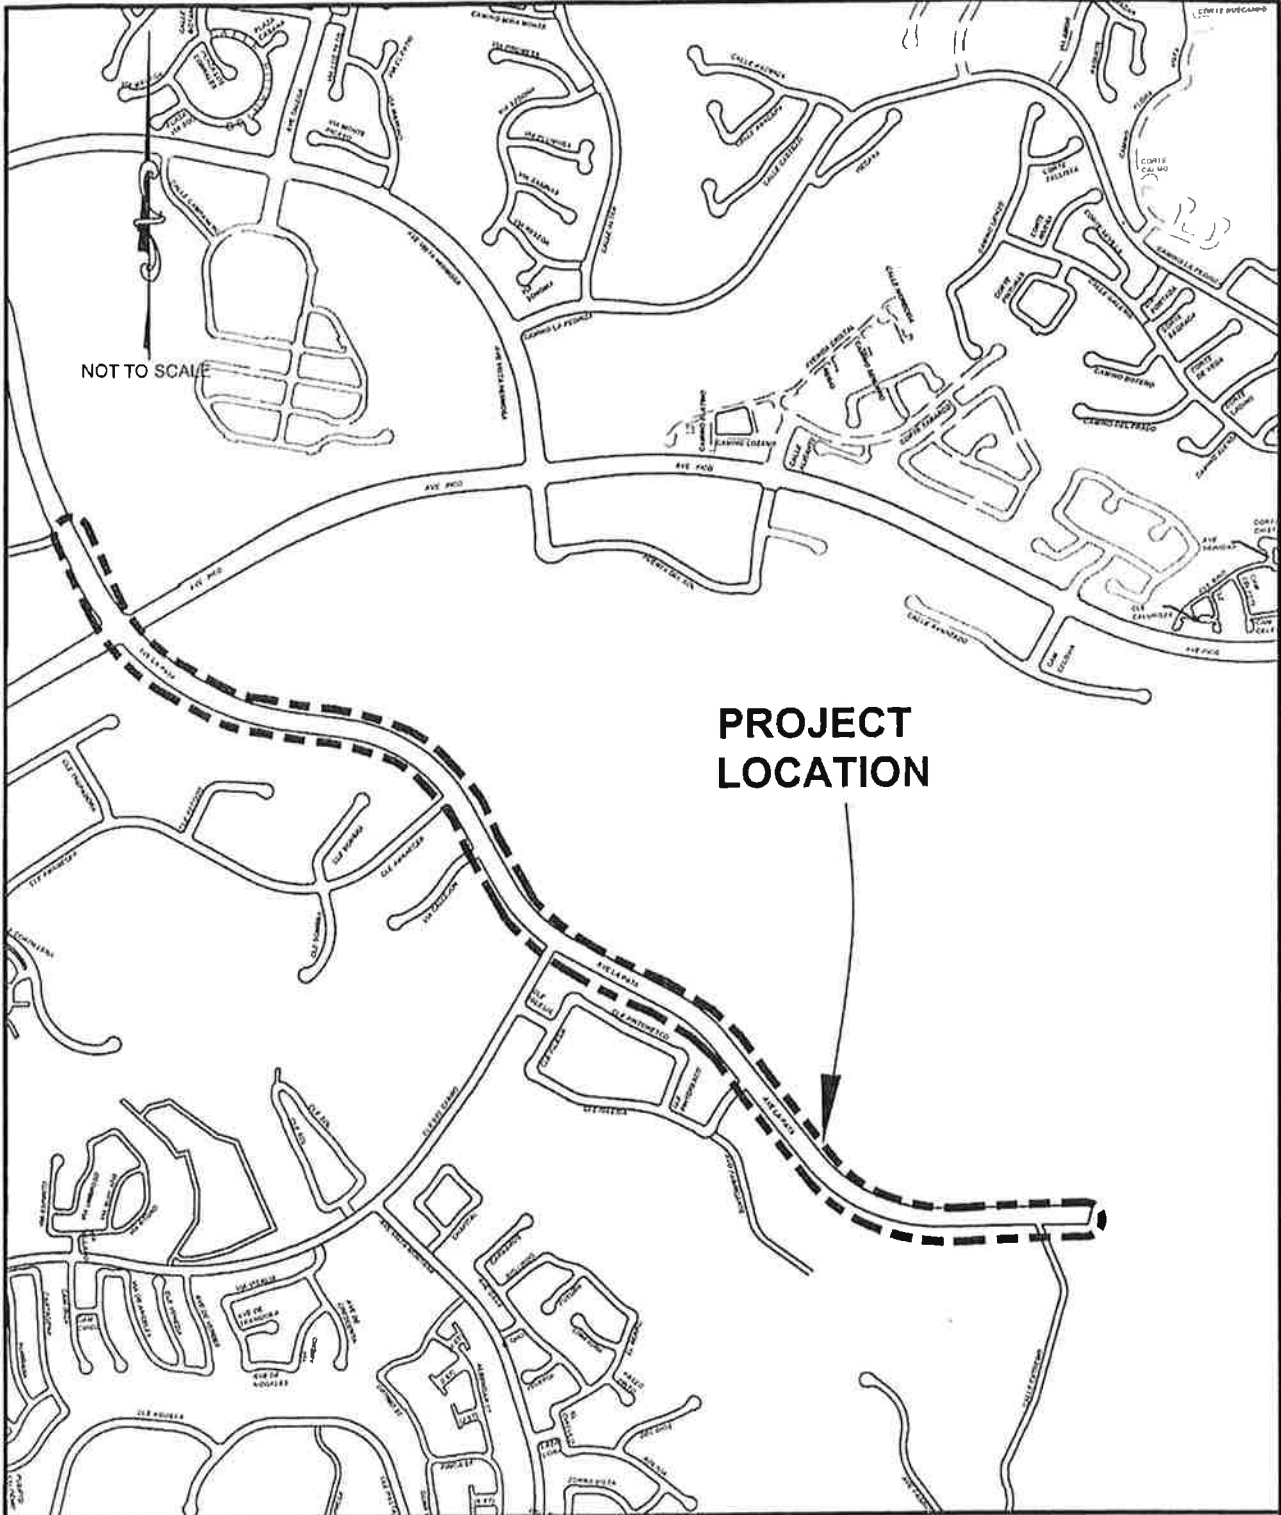

**PROJECT
LOCATION**



City of San Clemente

910 Calle Negocio, Suite 100
San Clemente, CA 92673
Tel (949) 361-8100
Fax (949) 361-8318

LOCATION MAP

Street Rehabilitation and Slurry Seal

For

Avenida La Pata

Via Onda to Calle Extremo

PROJECT NO. 16004

<p>Exempt recording requested by the City of San Clemente per Gov. Code Sec. 6103</p> <p>_____ City Clerk</p> <p>When Recorded Mail To:</p> <p>City Clerk City of San Clemente 100 Avenida Presidio San Clemente, CA 92672</p>	
--	--

Space above this line for Recorder's use

NOTICE OF COMPLETION

Notice is hereby given by the undersigned owner, a public entity of the State of California, that a public work of improvement has been completed as follows:

Project title or description of work: Street Rehabilitation and Slurry Seal for Avenida La Pata, (Via Onda to Calle Extremo)

Date of completion: January 29th 2016

Name of owner: City of San Clemente

Interest or estate of owner: Public Right-of-Way

Address of Owner: 100 Avenida Presidio

Name of contractor: All American Asphalt

Street address or legal description of site: Avenida La Pata from Via Onda to Calle Extremo

Dated: _____

Owner: City of San Clemente

Mayor _____

STATE OF CALIFORNIA)
COUNTY OF ORANGE) ss
CITY OF SAN CLEMENTE)

I am the City Clerk of the City of San Clemente, the public entity which executed the foregoing notice, and on whose behalf I make this verification: I have read said notice, know its contents, and the same is true. I certify under penalty of perjury that the foregoing is true and correct.

City Clerk _____

Dated this ____ day of _____, _____
